


Mar 6/13 Sandra Davis

1 of 3

Steve is scheduled in on Monday.

- Painters to come back after hardwood.
- Sue told H/O shoe mold would be supplied - we will supply & install per Heljar
- H/O removed tile in foyer & they will supply & install themselves tomorrow.
- H/O wants angle wall in foyer (not built yet) replaced w/ 5' straight wall from mark @ entry door. - Steve to do Mar 7 am.
- din room pillars are wider than arch. Box size of capital to ceiling in hall & ~~draw molding~~ box on dining room side
- entry closet has BDO sliders. S/O BDO swing doors. Reframe closet to 5'2" opening for 2 - 30" doors.
- mud room closet reframe for 1 - 30" door - series BDO.
- fireplace is not flush with marble top to bottom or side to side & gap between bottom & thres hold marble.
- H/O says "deco box" @ top of mantle "no flowers" per Cynthia is missing. She will have Cynthia send e-mail to us.
- H/O says we installed her range hood & that Bruno has paperwork specs for vent location. & says they brought Matt the specs for the vent location before brick went up. not in deal.
- H/O went to Carthier for glass corner doors (coppers)

- Carthier has 2 upper doors right of range & light valance left of range & 1 upper part of pantry door & pantry gable end (things in gable). "Mr kitchen guy"
- finish on stairs rough.
- H/O says there is supposed to be 2 closets & wet bar in basement. Says Bruno has paper - she says he said "Karen has to sign it". She says Bruno took a copy.
- Broken basement window with gap to outside s/e & n/e also
- Cleanup in basement not done - carpet not vacuumed & space under stairs not swept.
- bedroom over garage - 2 plug covers ~~missing~~ there but not installed.
- grout breaking out between tiles master ens.
- caulk tile @ master ens. shower curb.
- check all window frames for paint coverage.
- reclean bath sinks & ensure labels are removed.
- reclean all windows.
- install all bath ceiling vent covers.
- reframe closet in s/e corner bedroom for

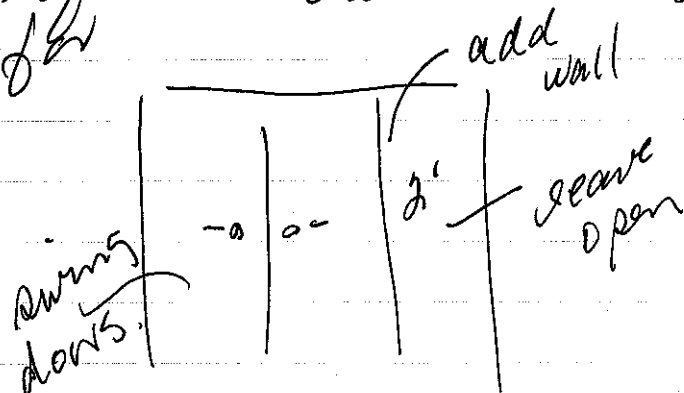

- H/O wants door from garage to back yd. not in deal.

- trim rings missing on left of lights.
- strip trim from front porch.

- no eaves troughs.
- ext columns & rail not done.
