

CONSTRUCTION SUMMARY

Lot: 2-1

Model: 31-02 B END2 Stanford Manor Project/Phase: The Manors at Pine Valley / 4

CROWN MOULDING

Invoi	ice	Qty.	Description
3	3120	1	GREAT ROOM: ADD 9 BOX WAFFLE CEILING - MODERN STYLE #CTR-B59
131	Nov23		
	NoCat		

TIT	-		7		_
Н.	H"	,.	I K I	[CA	

ELECTRICAL				
Invoice	Qty.	Description		
3120 164,749	8	BASEMENT REC ROOM: S/I 4" E/S LED INTERIOR POT LIGHT EACH. WHITE		
13Nov23		IN LIEU OF STANDARD CEILING LIGHTS, USE STANDARD SWITCHES. SEE PLAN FOR LOCATION		
3120 164,749	6	BASEMENT HALLWAY: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE		
13Nov23		IN LIEU OF STANDARD CEILING LIGHTS, USE STANDARD SWITCHES. SEE PLAN FOR LOCATION		
3120 164,749	4	MAIN HALL: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE		
13Nov23		IN LIEU OF STANDARD CEILING LIGHTS, USE STANDARD SWITCHES. SEE PLAN FOR LOCATION		
3120 164,749	3	MUD ROOM: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE		
13Nov23		IN LIEU OF STANDARD CEILING LIGHTS, USE STANDARD SWITCHES. SEE PLAN FOR LOCATION		
3120 164,749	5	KITCHEN: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE		
13Nov23		IN ADDITION TO STANDARD CEILING LIGHTS. SEE PLAN FOR LOCATION		
3120 164,752	1	KITCHEN: S/I ADDITIONAL INTERIOR SWITCH. SINGLE POLE		
13Nov23		FOR POTLIGHTS		
3120 164,741	1	KITCHEN: RELOCATE STANDARD CEILING MOUNT FIXTURE		
13Nov23		LOCATE APPROX CENTERED ABOVE ISLAND, SEE PLAN FOR LOCATION		
3120 164,753	1	KITCHEN: S/I ADDITIONAL REINFORCED CEILING OUTLET. SUPPORTS UP TO APPROX. 40 LBS.		
13Nov23		LOCATE APPROX CENTERED ABOVE ISLAND, ON SAME SWITCH AS STANDARD CEILING LIGHT. SEE PLAN FOR LOCATION		
3120 164,743	1	KITCHEN: S/I 110V WALL RECEPTACLE ON SEPARATE CIRCUIT		
13Nov23		FOR GAS APPLIANCE		
3120 164,749	8	GREAT ROOM: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE		
13Nov23		INCLUDED IN APS, SEE PLAN FOR LOCATION. INCLUDES 1 SWITCH		
3120 164,749	1	GREAT ROOM: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE		
13Nov23		ON SAME SWITCH AS OTHER POTLIGHTS. SEE PLAN FOR LOCATION		

Page 1 of 3



CONSTRUCTION SUMMARY

Lot: 2-1

Model: 31-02 B END2 Stanford Manor Project/Phase: The Manors at Pine Valley / 4

ELECTRICAL

Invoice	Qty.	Description
3120 164,743	GREAT ROOM: S/I 110V WALL RECEPTACLE ON SEPARATE CIRCUIT	
13Nov23		LOCATE APPROX 66" A.F.F., SEE PLAN FOR LOCATION
3120 164,749	1	POWDER ROOM: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE
13Nov23		IN ADDITION TO STANDARD LIGHT, ON SAME SWITCH. SEE PLAN FOR LOCATION
3120 164,749	5	UPPER HALL: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE
13Nov23		IN LIEU OF STANDARD CEILING LIGHTS, USE STANDARD SWITCHES. SEE PLAN FOR LOCATION
3120 164,749	4	PRINCIPAL BEDROOM: S/I 4" E/S LED INTERIOR POT LIGHT - EACH. WHITE
13Nov23		IN ADDITION TO STANDARD CEILING LIGHTS. SEE PLAN FOR LOCATION
3120 164,752	1	PRINCIPAL BEDROOM: S/I ADDITIONAL INTERIOR SWITCH. SINGLE POLE
13Nov23		FOR POTLIGHTS
3120 164,761	1	PRINCIPAL ENSUITE: S/I SHOWER POT LIGHT: 4 INCH RECESSED SHOWER POT LIGHT COMPLETE WITH SWITCH
13Nov23		IN ADDITION TO STANDARD SHOWER POTLIGHT, ON SAME SWITCH
3120 164,747	1	GARAGE: S/I 240V (50 AMP) RECEPTACLE ON A SEPARATE CIRCUIT
13Nov23		FOR FUTURE CAR CHARGER

FORMING

1	nvoice	Qty.	Description
	3119	1	BASEMENT: S/I BACK -FLOW PREVENTER VALVE (BASEMENT)
	164,803		
	13Nov23		

FRAMING

Invoice	Qty.	Description
3120 164,770 13Nov23	1	KITCHEN: DELETE KITCHEN BULKHEAD, IF POSSIBLE, SITE APPROVAL REQUIRED AND IF MECHANICAL LAYOUTS ALLOW. GAP ABOVE UPPER KITCHEN CABINETS WILL BE PRESENT UNLESS ADDITIONAL CABINETRY IS PURCHASED.
3120 164,775 13Nov23	1	KITCHEN: S/I TALLER UPPER, FURRING PANEL WITH CROWN MOULDING TO CEILING. OPTION ONLY AVAILBLE WITH DELETED BULKHEAD.
3120 164,774 13Nov23	1	PRINCIPAL ENSUITE: S/I RECESSED SHOWER NICHE [SHAMPOO SHELF] - COMPLETE WITH MATCHING STONE ON 4 SIDES, STANDARD TILE, APPROX. 12 X 42 INSTALLED VERTICALLY WITH STONE SHELF DIVIDERS. BASED ON STANDARD FINISHES.

Page 2 of 3



CONSTRUCTION SUMMARY

Lot: 2-1

Model: 31-02 B END2 Stanford Manor Project/Phase: The Manors at Pine Valley / 4

w	•	•	7	A	-	~
L		•	/	Λ		

Invoice	Qty.	Description
3120 164,780	1	KITCHEN: GAS LINE ROUGH-IN - MAIN FLOOR FOR APPLIANCE
13Nov23		

INTERIOR DOORS AND TRIM

Invoice	Qty.	Description
3120 164,784 13Nov23	* *	2ND FLOOR: S/I 8FT HIGH DOOR THROUGHOUT SECOND FLOOR IN LIEU OF STANDARD HEIGHT DOOR. PRICE IS PER DOOR

NETWORK AND WIRING

Invoice Qty. Description				
3120 164,787 13Nov23	1	GREAT ROOM: S/I ADDITIONAL CAT6 ETHERNET OUTLET SEE PLAN FOR LOCATION		
3120	1	GREAT ROOM: S/I CONDUIT PIPE FOR WALL MOUNT TV LOCATED APPROX. 66" A.F.F. ABOVE FIREPLACE TO		
164,789 13Nov23		CABLE LOCATION. SEE PLAN FOR LOCATION.		
3120 164,794 13Nov23	1	EXTERIOR: S/I SECURITY PACKAGE - ROUGH - IN WIRING FOR: 1 RING DOOR BELL + 2 CAMERAS - 1 AT FRONT AND 1 AT REAR. COMPONENTS NOT INCLUDED. (CAT6)		

PLUMBING

Invoice	Qty.	Description
3120 164,798 13Nov23	1	KITCHEN: S/I ROUGH-IN 1/4" COLD WATER LINE TO FRIDGE
3120	1	PRINCIPAL ENSUITE: UPGRADE TO MOEN 'ALIGN' SUITE INCLUDING RAIN SHOWER + TUB FILLER + LAV FAUCETx2
13Nov23 NoCat		

WINDOWS - BASEMENT

Invoice	Qty.	Description
3119 164,802 13Nov23		BASEMENT: S/I BASEMENT WINDOW SIZE 30" X 24" IN LIEU OF STANDARD - WHITE. WINDOW WELLS MAY BE REQUIRED.

DisciplineMS.rpt 23feb21

THEMANORS

The Stanford Manor 3-4 BEDROOMS | 4.5 BATHROOMS

ELEV. A 2922 SQ.FT. INCLUDES 887 SQ.FT. OF FINISHED BASEMENT

ELEV. B 2926 sq.ft. INCLUDES 687 SQ.FT. OF FINISHED BASEMENT

TM- 2-1

NOV 8 2023


END 1 A 2967 sq.ft. INCLUDES 694 SQ.FT. OF FINISHED BASEMEN

END 1 B 2970 sq.ft. INCLUDES 694 SQ.FT. OF FINISHED BASEMENT

END 2 A 2954 SO.FT. INCLUDES 695 SO.FT. OF FINISHED BASEMENT

END 2 B 2954 SQ.FT. INCLUDES 695 SQ.FT. OF FINISHED BASEMENT

CORNER A 2967 SQ.FT. INCLUDES 694 SQ.FT. OF FINISHED BASEMENT

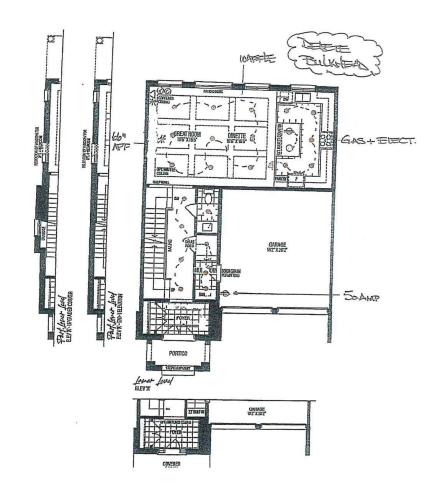

THE MANORS

The Stanford Manor 3-4 BEDROOMS | 4.5 BATHROOMS

ELEV. A 2922 SQ.FT. INCLUDES 687 SQ.FT. OF FINISHED BASEMENT

ELEV. B 2926 sq.ft. INCLUDES 687 SQ.FT. OF FINISHED BASEMENT

TM- 2-1

Nov 9 2025


END 1 A 2967 sq.ft. INCLUDES 694 SQ.FT. OF FINISHED BASEMENT

END 1 B 2970 SQ.FT. INCLUDES 694 SQ.FT. OF FINISHED BASEMENT END 2 A 2954 sq.ft. INCLUDES 695 SQ.FT. OF FINISHED BASEMENT

END 2 B 2954 sq.ft. INCLUDES 695 SQ.FT. OF FINISHED BASEMENT

CORNER A 2967 sq.ft. INCLUDES 694 SQ.FT. OF FINISHED BASEMENT



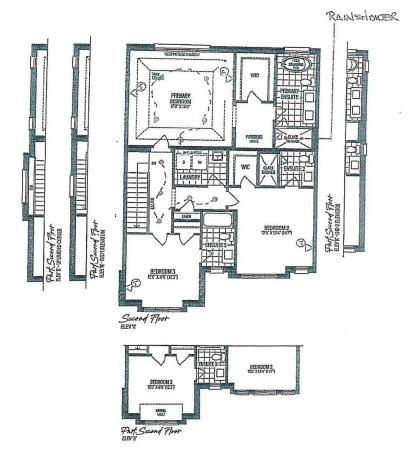

THE MANORS

AT FIRE VALUE.

ELEV. A 2922 SQ.FT. INCLUDES 687 SQ.FT. OF FINISHED BASEMENT

ELEV. B 2926 sq.ft. INCLUDES 687 SQ.FT. OF FINISHED BASEMENT

TM- 2-1 NOU 9 2023. The Stanford Manor 3-4 BEDROOMS | 4.5 BATHROOMS


END 1 A 2967 SQ.FT. INCLUDES 694 SQ.FT. OF FINISHED BASEMENT

END 1 B 2970 sq.ft.

END 2 A 2954 SQ.FT. INCLUDES 695 SQ.FT. OF FINISHED BASEMENT

END 2 B 2954 sq.ft. INCLUDES 695 SQ.FT. OF FINISHED BASEMENT

CORNER A 2967 sq.ft. INCLUDES 694 Sq.Ft. OF FINISHED BASEMENT

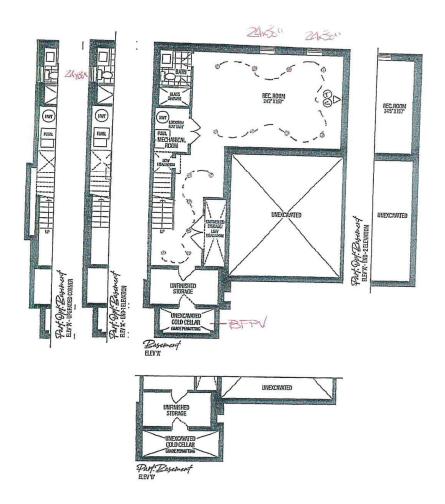



PLUMBING UPGRADES

ALIGN

Ceiling Mount: 226651 (12" Arm)			
		Brushed Gold	J
		Brushed Nickel	
		Chrome	
		Matte Black	
Date: Nov. 9 2023		Lot: TM- 2-1	
Location: Principal Ensuite	Š		
Signature:		Signature:	

Shower with 3-Function Transfer Valve/Trim and Slide Bar with Hand Shower + 7" Rain Showerhead From Ceiling on 12" Arm

(includes plumbing provision for ceiling mount showerhead) Model T2192EP/UT4191/3887EP/226651/S176/U361CI/ 62320/A725





ALIGN



*includes Tub Drain Half Kit

Brushed Gold
Brushed Nickel

	Chrome Matte Black	
Date: Nov 9 2023	Lot: TM- 2-1	
Location: Principal Ensuite		
Signature:	Signature:	



V



ALIGN



	Brushed Gold Brushed Nickel Chrome Matte Black	□ ×2 □ □
Date: Nov 9 2023	Lot: TM- 2-1	
Location: Principal Gnovite		
Signature:	Signature:	

